



School A K-8 School, Pace, FL
Weather Delay Log September 2021

As shown in the attached data, we experienced schedule impacts due to rain this month. There were a total of ten (10) days with measurable rainfall over .1", compared to a 30-year average of nine (9) [see 00073-3.B]. This number does not account for further delays caused on subsequent days to dewater work areas. This rainfall impacted the clearing and grading of our parking lot, digging and pouring of foundation footers at Building F, and layout of underground electrical at the Chiller Yard. We have worked the past two Saturdays to try to minimize the impact of the weather delays.

We are requesting one (1) calendar days be added to the contract date. Thank you.

Stephen Feher
Project Manager

THERE IS NO ASSOCIATED WEBCAM
WITH THIS STATION

Weather History for KFLPACE24

Summary
September 1, 2021 - September 30, 2021

	High	Low	Average
Temperature	94.5 °F	55.2 °F	74.9 °F
Dew Point	81.9 °F	48.9 °F	69.2 °F
Humidity	99 %	34 %	85 %
Precipitation	9.80 in	--	--

	High	Low	Average
Wind Speed	19.2 mph	0.0 mph	1.7 mph
Wind Gust	23.9 mph	--	2.2 mph
Wind Direction	--	--	SE
Pressure	29.98 in	29.54 in	--

Graph	Table
-------	-------

September 1, 2021 - September 30, 2021

Date	Temperature			Dew Point			Humidity			Speed			Pressure		Precip. Accum.
	High	Avg	Low	High	Avg	Low	High	Avg	Low	High	Avg	Low	High	Low	Sum
9/1/2021	94.5 °F	88.2 °F	82.0 °F	79.9 °F	76.9 °F	70.7 °F	86 %	70 %	49 %	11.6 mph	3.9 mph	0.0 mph	29.61 in	29.54 in	0.00 in
9/10/2021	86.4 °F	75.0 °F	65.3 °F	66.2 °F	61.9 °F	54.0 °F	91 %	67 %	35 %	9.2 mph	1.7 mph	0.0 mph	29.83 in	29.74 in	0.00 in
9/11/2021	92.1 °F	75.5 °F	62.6 °F	72.3 °F	66.2 °F	59.2 °F	98 %	76 %	39 %	11.2 mph	1.4 mph	0.0 mph	29.93 in	29.80 in	0.00 in
9/12/2021	90.3 °F	77.6 °F	70.3 °F	77.4 °F	73.4 °F	70.0 °F	99 %	88 %	58 %	10.3 mph	1.2 mph	0.0 mph	29.98 in	29.89 in	0.24 in
9/13/2021	84.6 °F	76.3 °F	71.6 °F	79.2 °F	73.8 °F	70.5 °F	99 %	93 %	66 %	15.7 mph	1.0 mph	0.0 mph	29.96 in	29.81 in	0.00 in
9/14/2021	84.4 °F	77.0 °F	72.5 °F	78.3 °F	74.2 °F	72.1 °F	99 %	92 %	71 %	4.5 mph	0.3 mph	0.0 mph	29.83 in	29.70 in	0.12 in
9/15/2021	73.9 °F	72.6 °F	71.2 °F	73.6 °F	72.3 °F	70.9 °F	99 %	99 %	98 %	10.7 mph	0.7 mph	0.0 mph	29.70 in	29.57 in	4.46 in
9/16/2021	88.2 °F	77.1 °F	72.1 °F	81.0 °F	74.9 °F	71.8 °F	99 %	93 %	72 %	9.2 mph	1.1 mph	0.0 mph	29.74 in	29.59 in	1.24 in
9/17/2021	86.7 °F	77.8 °F	73.6 °F	79.5 °F	75.7 °F	73.2 °F	99 %	94 %	74 %	9.8 mph	1.0 mph	0.0 mph	29.84 in	29.70 in	1.73 in
9/18/2021	86.7 °F	77.7 °F	73.0 °F	78.1 °F	75.4 °F	72.1 °F	99 %	93 %	69 %	9.2 mph	0.5 mph	0.0 mph	29.83 in	29.72 in	0.10 in
9/19/2021	86.9 °F	75.8 °F	72.3 °F	80.1 °F	74.3 °F	71.4 °F	99 %	95 %	73 %	5.1 mph	0.3 mph	0.0 mph	29.79 in	29.68 in	0.27 in
9/20/2021	86.7 °F	77.1 °F	72.7 °F	80.3 °F	75.1 °F	72.1 °F	99 %	94 %	73 %	12.8 mph	0.7 mph	0.0 mph	29.76 in	29.68 in	1.32 in
9/21/2021	91.4 °F	78.4 °F	70.5 °F	81.9 °F	74.0 °F	70.2 °F	99 %	88 %	57 %	8.5 mph	1.2 mph	0.0 mph	29.83 in	29.71 in	0.17 in
9/22/2021	79.3 °F	72.4 °F	59.4 °F	74.1 °F	67.8 °F	57.2 °F	99 %	86 %	63 %	17.2 mph	5.4 mph	0.0 mph	29.79 in	29.68 in	0.00 in
9/23/2021	76.3 °F	64.7 °F	55.8 °F	59.4 °F	55.0 °F	48.9 °F	99 %	73 %	41 %	19.2 mph	4.5 mph	0.0 mph	29.82 in	29.73 in	0.00 in
9/24/2021	80.4 °F	65.8 °F	55.2 °F	61.9 °F	55.3 °F	50.0 °F	94 %	72 %	38 %	13.2 mph	2.7 mph	0.0 mph	29.86 in	29.76 in	0.00 in
9/25/2021	83.5 °F	67.6 °F	55.8 °F	64.9 °F	56.5 °F	50.4 °F	92 %	71 %	34 %	11.4 mph	2.5 mph	0.0 mph	29.87 in	29.76 in	0.00 in
9/26/2021	89.2 °F	71.5 °F	59.5 °F	67.6 °F	61.1 °F	56.8 °F	97 %	73 %	36 %	8.5 mph	1.5 mph	0.0 mph	29.90 in	29.78 in	0.00 in
9/27/2021	87.3 °F	73.1 °F	61.3 °F	73.0 °F	66.8 °F	60.7 °F	99 %	83 %	49 %	10.5 mph	1.4 mph	0.0 mph	29.87 in	29.77 in	0.00 in
9/28/2021	86.0 °F	74.1 °F	66.6 °F	75.7 °F	71.0 °F	66.2 °F	99 %	91 %	66 %	7.8 mph	1.1 mph	0.0 mph	29.80 in	29.70 in	0.00 in
9/29/2021	86.4 °F	75.7 °F	69.6 °F	74.7 °F	70.9 °F	67.6 °F	99 %	86 %	60 %	11.2 mph	1.9 mph	0.0 mph	29.79 in	29.71 in	0.15 in
9/30/2021	90.1 °F	76.1 °F	69.3 °F	73.9 °F	70.2 °F	66.5 °F	99 %	84 %	51 %	6.9 mph	0.8 mph	0.0 mph	29.85 in	29.75 in	0.00 in



Culpepper Construction Company
Job #: 21006 Santa Rosa School A
3354 Wallace Lake Road
Pace, Florida 32571
8504454824

Monthly Weather Delay Report

Weather Log

Date	Delay	Sky	Precipitation	Measured Temperature Avg	Measured Wind Speed Gusts	Comments
09/14/2021		Rain	.12	78	8	
09/15/2021	Yes	Rain	4.46	72	11	J Miller, Barnes Electric and Bayside Structures all showed up to work this morning and were rained out. We have received heavy rains on site all day. Roughly 3.5".
09/17/2021	Yes	Rain	1.73	76	12	No work on site today due to rain. Major wash-out at the retention pond due to silt fence being removed by Panhandle's fence contractor
09/20/2021		Rain	1.32	77	13	Its been raining sporadically on and off all day.
09/21/2021		Rain	.17	78	8	
09/29/2021		Rain	.15	75	10	

Elev 0 ft, 30.68 °N, 87.18 °W

3354 Wallace Lake Road - KFLPACE24 ⓘ

FORECAST FOR PACE, FL (/WEATHER/US/FL/PACE/KFLPACE24)

Station Summary

Online(updated 32 seconds ago)

CURRENT CONDITIONS

MAP



86.4 °F
Feels Like 92.3 °



WIND & GUST
0.7 / 1.1 mph

DEWPOINT
71.4 ° F


PRECIP RATE
0.00 in/hr

PRESSURE
29.84 in

HUMIDITY
61 %

PRECIP ACCUM
0.00 in

UV
0

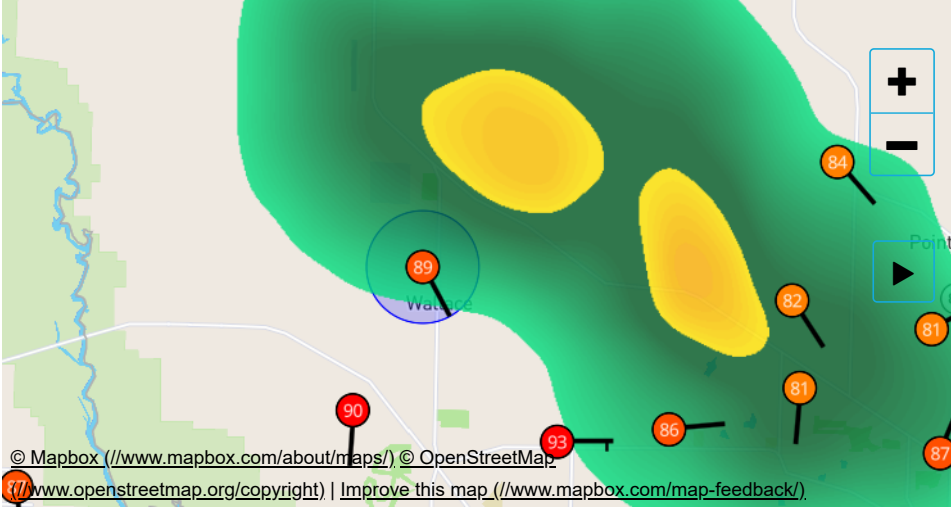

lat=30.687840440032158&lon=-87.17004201081193&zoom=13&tl.play=0&tl.spd=2&groupSevere

PWS CURRENT CONDITIONS

TEMPERATURE



WIND



PRESSURE



CURRENT
86°

DEWPOINT
71.4 °F
HUMIDITY
61 %



WIND FROM
SE
GUST
1.1 mph

CURRENT
29.84 In


PRECIPITATION




UV



SOLAR RADIATION



PRECIP RATE
0.00 in/hr
PRECIP TOTAL
0.00 in



CURRENT UV
0
UV RISK



CURRENT
92.70 watts/m²

ASSOCIATED WEBCAM

THERE IS NO ASSOCIATED WEBCAM
WITH THIS STATION

Weather History for KFLPACE24

Summary
September 1, 2021 - September 30, 2021

	High	Low	Average
Temperature	94.5 °F	55.2 °F	74.9 °F
Dew Point	81.9 °F	48.9 °F	69.2 °F
Humidity	99 %	34 %	85 %
Precipitation	9.80 in	--	--

	High	Low	Average
Wind Speed	19.2 mph	0.0 mph	1.7 mph
Wind Gust	23.9 mph	--	2.2 mph
Wind Direction	--	--	SE
Pressure	29.98 in	29.54 in	--

Graph	Table
-------	-------

September 1, 2021 - September 30, 2021

Date	Temperature			Dew Point			Humidity			Speed			Pressure		Precip. Accum.
	High	Avg	Low	High	Avg	Low	High	Avg	Low	High	Avg	Low	High	Low	Sum
9/1/2021	94.5 °F	88.2 °F	82.0 °F	79.9 °F	76.9 °F	70.7 °F	86 %	70 %	49 %	11.6 mph	3.9 mph	0.0 mph	29.61 in	29.54 in	0.00 in
9/10/2021	86.4 °F	75.0 °F	65.3 °F	66.2 °F	61.9 °F	54.0 °F	91 %	67 %	35 %	9.2 mph	1.7 mph	0.0 mph	29.83 in	29.74 in	0.00 in
9/11/2021	92.1 °F	75.5 °F	62.6 °F	72.3 °F	66.2 °F	59.2 °F	98 %	76 %	39 %	11.2 mph	1.4 mph	0.0 mph	29.93 in	29.80 in	0.00 in
9/12/2021	90.3 °F	77.6 °F	70.3 °F	77.4 °F	73.4 °F	70.0 °F	99 %	88 %	58 %	10.3 mph	1.2 mph	0.0 mph	29.98 in	29.89 in	0.24 in
9/13/2021	84.6 °F	76.3 °F	71.6 °F	79.2 °F	73.8 °F	70.5 °F	99 %	93 %	66 %	15.7 mph	1.0 mph	0.0 mph	29.96 in	29.81 in	0.00 in
9/14/2021	84.4 °F	77.0 °F	72.5 °F	78.3 °F	74.2 °F	72.1 °F	99 %	92 %	71 %	4.5 mph	0.3 mph	0.0 mph	29.83 in	29.70 in	0.12 in
9/15/2021	73.9 °F	72.6 °F	71.2 °F	73.6 °F	72.3 °F	70.9 °F	99 %	99 %	98 %	10.7 mph	0.7 mph	0.0 mph	29.70 in	29.57 in	4.46 in
9/16/2021	88.2 °F	77.1 °F	72.1 °F	81.0 °F	74.9 °F	71.8 °F	99 %	93 %	72 %	9.2 mph	1.1 mph	0.0 mph	29.74 in	29.59 in	1.24 in
9/17/2021	86.7 °F	77.8 °F	73.6 °F	79.5 °F	75.7 °F	73.2 °F	99 %	94 %	74 %	9.8 mph	1.0 mph	0.0 mph	29.84 in	29.70 in	1.73 in
9/18/2021	86.7 °F	77.7 °F	73.0 °F	78.1 °F	75.4 °F	72.1 °F	99 %	93 %	69 %	9.2 mph	0.5 mph	0.0 mph	29.83 in	29.72 in	0.10 in
9/19/2021	86.9 °F	75.8 °F	72.3 °F	80.1 °F	74.3 °F	71.4 °F	99 %	95 %	73 %	5.1 mph	0.3 mph	0.0 mph	29.79 in	29.68 in	0.27 in
9/20/2021	86.7 °F	77.1 °F	72.7 °F	80.3 °F	75.1 °F	72.1 °F	99 %	94 %	73 %	12.8 mph	0.7 mph	0.0 mph	29.76 in	29.68 in	1.32 in
9/21/2021	91.4 °F	78.4 °F	70.5 °F	81.9 °F	74.0 °F	70.2 °F	99 %	88 %	57 %	8.5 mph	1.2 mph	0.0 mph	29.83 in	29.71 in	0.17 in
9/22/2021	79.3 °F	72.4 °F	59.4 °F	74.1 °F	67.8 °F	57.2 °F	99 %	86 %	63 %	17.2 mph	5.4 mph	0.0 mph	29.79 in	29.68 in	0.00 in
9/23/2021	76.3 °F	64.7 °F	55.8 °F	59.4 °F	55.0 °F	48.9 °F	99 %	73 %	41 %	19.2 mph	4.5 mph	0.0 mph	29.82 in	29.73 in	0.00 in
9/24/2021	80.4 °F	65.8 °F	55.2 °F	61.9 °F	55.3 °F	50.0 °F	94 %	72 %	38 %	13.2 mph	2.7 mph	0.0 mph	29.86 in	29.76 in	0.00 in
9/25/2021	83.5 °F	67.6 °F	55.8 °F	64.9 °F	56.5 °F	50.4 °F	92 %	71 %	34 %	11.4 mph	2.5 mph	0.0 mph	29.87 in	29.76 in	0.00 in
9/26/2021	89.2 °F	71.5 °F	59.5 °F	67.6 °F	61.1 °F	56.8 °F	97 %	73 %	36 %	8.5 mph	1.5 mph	0.0 mph	29.90 in	29.78 in	0.00 in
9/27/2021	87.3 °F	73.1 °F	61.3 °F	73.0 °F	66.8 °F	60.7 °F	99 %	83 %	49 %	10.5 mph	1.4 mph	0.0 mph	29.87 in	29.77 in	0.00 in
9/28/2021	86.0 °F	74.1 °F	66.6 °F	75.7 °F	71.0 °F	66.2 °F	99 %	91 %	66 %	7.8 mph	1.1 mph	0.0 mph	29.80 in	29.70 in	0.00 in
9/29/2021	86.4 °F	75.7 °F	69.6 °F	74.7 °F	70.9 °F	67.6 °F	99 %	86 %	60 %	11.2 mph	1.9 mph	0.0 mph	29.79 in	29.71 in	0.15 in
9/30/2021	90.1 °F	76.1 °F	69.3 °F	73.9 °F	70.2 °F	66.5 °F	99 %	84 %	51 %	6.9 mph	0.8 mph	0.0 mph	29.85 in	29.75 in	0.00 in

[About Us \(/about/our-company\)](#)

[Contact \(/about/contact-us\)](#)

[Careers \(http://ibm.biz/BdH3av\)](#)

[PWS Network \(/pws/overview\)](#)

[WunderMap \(/wundermap\)](#)

[Feedback & Support \(https://www.wunderground.com/feedback\)](#)


[Terms of Use \(/company/legal\)](#)

[Privacy Policy \(/company/privacy-policy\)](#)

[Accessibility Statement \(/accessibility-statement\)](#)

[AdChoices \(/company/ad-choices\)](#)

[Data Vendors \(/data-vendors\)](#)

 (https://www.essentialaccessibility.com/the-weather-channel?utm_source=theweatherchannelhomepage&utm_medium=iconlarge&utm_term=eachannelpage&utm_content=header&utm_campaign=theweatherchannel)

We recognize our responsibility to use data and technology for good. Take control of your data.

[Privacy Settings \(/privacy-settings\)](#) | [Review My Advertising Settings \(/privacy-settings#do-not-sell\)](#) | [Data Rights \(/data-rights\)](#)

Powered by the IBM Cloud (<https://www.ibm.com/cloud/>)





Culpepper Construction Company
 Job #: 21006 Santa Rosa School A
 3354 Wallace Lake Road
 Pace, Florida 32571
 8504454824

Daily Weather Logs

Weather Log

Date	Delay	Sky	Precipitation	Measured Temperature High	Measured Temperature Low	Measured Wind Speed Gusts	Comments	Created By
09/30/2021				84	69	7		
09/29/2021		Rain	.15	82	69	10		
09/28/2021				83	66	9		
09/27/2021				85	61	9		
09/26/2021				84	58	8		
09/24/2021				78	53	6		
09/23/2021				74	54	11		
09/22/2021				79	64	17		
09/21/2021		Rain	.17	87	71	8		
09/20/2021		Rain	1.32	83	72	13	Its been raining sporadically on and off all day.	
09/18/2021				81	74	7		
09/17/2021	Yes	Rain	1.73	82	73	12	No work on site today due to rain. Major wash-out at the retention pond due to silt fence being removed by Panhandle's fence contractor	
09/16/2021				81	73	13		
09/15/2021	Yes	Rain	4.46	73	71	11	J Miller, Barnes Electric and Bayside Structures all showed up to work this morning and were rained out. We have received heavy rains on site all day. Roughly 3.5".	
09/14/2021		Rain	.12	85	72	8		
09/13/2021				80	71	18		
09/12/2021				86	71	10		
09/11/2021				87	62	11		
09/10/2021				85	62	10		
09/09/2021				84	70	10		
09/08/2021				82	74	7		



Culpepper Construction Company
Job #: 21006 Santa Rosa School A
3354 Wallace Lake Road
Pace, Florida 32571
8504454824

Date	Delay	Sky	Precipitation	Measured Temperature High	Measured Temperature Low	Measured Wind Speed Gusts	Comments	Created By
09/07/2021				89	72	14		
09/06/2021				90	71	11		
09/05/2021				86	72	8		
09/04/2021				87	70	11		
09/03/2021				89	70	10		
09/02/2021				88	71	7		
09/01/2021				91	72	13		



Culpepper Construction Company
 Job #: 21006 Santa Rosa School A
 3354 Wallace Lake Road
 Pace, Florida 32571
 8504454824

Manpower Log

Group	Company	Workers	Comments
Date: 09/30/2021			
	COMFORT SYSTEMS USA, INC.	2	Comfort Systems received and installed the three grease traps on the south side of building F.
	J MILLER CONSTRUCTION, INC.	9	J Miller continued to pour curb on the north end of the parking lot.
	BARNES ELECTRIC COMPANY, INC.	3	Barnes continued installing conduit for the light poles in the parking lot. They also set up a temporary panel on the south end of Building F.
	BAYSIDE STRUCTURES, LLC	3	Bayside continued excavating F.3 and F.C line. They put forms and steel in the F.8 line.
	THE WALLACE COMPANY	5	The Wallace Company continued putting irrigation sleeves in at the parking lot.
		1	
Date: 09/29/2021			
	THE WALLACE COMPANY	4	The Wallace Company began putting in their irrigation sleeves that run underneath the parking lot.
	J MILLER CONSTRUCTION, INC.	11	J Miller continued to pour curb in the parking lot. They started forming some of the radius's.
	BAYSIDE STRUCTURES, LLC	5	Bayside poured the footings for the Chiller Pad and continued excavating along the F.8 line.
	BARNES ELECTRIC COMPANY, INC.	3	Barnes started burying conduit for the light poles in the parking lot.
		1	
Date: 09/28/2021			
	J MILLER CONSTRUCTION, INC.	8	J Miller continued to pour parking lot curb. They also extended and freshened up the eastward construction entrance.
	BAYSIDE STRUCTURES, LLC	5	Bayside continued to excavate along the F.8 gridline of Building F. They also placed forms and rebar in the chiller pad footings for tomorrows pour.
	BARNES ELECTRIC COMPANY, INC.	3	Barnes continued to lay and bury conduit for the primary power and temporary power feeding the building.
	COMFORT SYSTEMS USA, INC.	2	Comfort Systems finished excavating for their grease traps. Structures are scheduled to be delivered and set this Thursday.
Date: 09/27/2021			
	COMFORT SYSTEMS USA, INC.	2	Began excavating holes for grease traps. Laid out the location of the precast structures.



Culpepper Construction Company
 Job #: 21006 Santa Rosa School A
 3354 Wallace Lake Road
 Pace, Florida 32571
 8504454824

Group	Company	Workers	Comments
	BARNES ELECTRIC COMPANY, INC.	3	Continued burying conduit for primary power to building with temporary power lines.
	BAYSIDE STRUCTURES, LLC	5	Continued excavating and laying out footings along F.8 line of Building F.
	J MILLER CONSTRUCTION, INC.	12	J Miller began pouring curb in the parking lot. They poured all of the straight runs within the interior bays.
Date: 09/24/2021			
	BARNES ELECTRIC COMPANY, INC.	2	Barnes turned primary pipes up at their tap box and installed bonding at Building F footing.
	BAYSIDE STRUCTURES, LLC	4	Poured 50 yards of concrete making up the footings on the south end of Building F and (2) pads.
	J MILLER CONSTRUCTION, INC.	4	J Miller started regrade out parking lot washed out by rain from the previous week.
Date: 09/23/2021			
	BARNES ELECTRIC COMPANY, INC.	2	Finished excavating and installing conduit for PIV running east to west across the parking lot.
	BAYSIDE STRUCTURES, LLC	4	Bayside continued cutting footings along Building F and installing rebar in footings previously cut. Concrete pour planned for tomorrow afternoon.
	J MILLER CONSTRUCTION, INC.	4	J Miller continued to stake out remaining curb around parent pick up road.
Date: 09/22/2021			
	BAYSIDE STRUCTURES, LLC	4	Continue to excavate foundations at Building F. Layout grid lines for Building F footings and continued to form footings along F.A. line and form stand alone foundations on F.B. line. Began to install rebar in footings.
	BARNES ELECTRIC COMPANY, INC.	2	Excavated trench across parking lot and installed conduit for PIV.
	J MILLER CONSTRUCTION, INC.	2	J Miller continued to install pins and string lines for curb on the north end of the parking lot. We installed the section of the fire main running east to west across the parking lot.
Date: 09/21/2021			
	BAYSIDE STRUCTURES, LLC	4	Bayside continued to excavate foundations in Building F. Set up control points from surveyors, layout footings at Building F. Continue to make up forms for foundations.
	BARNES ELECTRIC COMPANY, INC.	2	Barnes started burying conduit for primary power running to transformers and laid out location of PIV under the parking lot.
	J MILLER CONSTRUCTION, INC.	2	J Miller set up pins and string lines at curbs around parking lot.
Date: 09/20/2021			
	BARNES ELECTRIC	3	Barnes Electric set up the sump pump south of the building pad to drain some water ponding in their trenching area. They also built the temporary panel and back board for the



Culpepper Construction Company
 Job #: 21006 Santa Rosa School A
 3354 Wallace Lake Road
 Pace, Florida 32571
 8504454824

Group	Company	Workers	Comments
	COMPANY, INC.		building power.
	BAYSIDE STRUCTURES, LLC	4	Bayside continued to build forms and cut footings for the CMU wall at the chiller yard.
	GULF FENCE & CONSTRUCTION CO	2	Gulf Fence has 100% of the post set and now have about 75% of the wire pulled for the permanent fence.
		1	
Date: 09/16/2021			
	BAYSIDE STRUCTURES, LLC	2	Received and unloaded miscellaneous material. Rained out around 8:30am.
	BARNES ELECTRIC COMPANY, INC.	2	Barnes Electric ran conduit and pulled wire to Baysides office trailer.
Date: 09/15/2021			
	BARNES ELECTRIC COMPANY, INC.	2	Barnes was rained out of working in the field so they stayed in the office trailer and worked on a material buy list, held a crew safety meeting and looked into hooking up temporary power to Baysides jobsite trailer.
	BAYSIDE STRUCTURES, LLC	2	Bayside started staging rebar around the chiller yard pad and was soon rained out.
	J MILLER CONSTRUCTION, INC.	4	J Miller laid out the curb on the northern end of the parking lot and were eventually rained out.
Date: 09/14/2021			
	BARNES ELECTRIC COMPANY, INC.	2	Barnes laid out both transformer pad locations at the chiller yard. Dropped off material and mini excavator.
	J MILLER CONSTRUCTION, INC.	3	J Miller continued to bring in several truck loads of dirt to build of the bus ramp area as well as the north parking lot. They compacted the curb base in preparation of forming curbs later this week.
	GULF FENCE & CONSTRUCTION CO	4	Continued installing permanent fence along the north property line.
	BAYSIDE STRUCTURES, LLC	2	Bayside dropped off several loads of material on site as well as equipment. Their crew laid out and started digging the footings around the chiller yard.
Date: 09/13/2021			
	J MILLER CONSTRUCTION, INC.	4	Continue grading north and east ends of the parking lot. Brought in several dump trucks of fill to build up low spots in road around parking lot. Laid out 4 corners of CMU wall at Chiller Yard.
	GULF FENCE & CONSTRUCTION CO	4	Continued setting post along the north side of the property. Started pulling wire for the permanent fence along Chumuckla Highway.
	BARNES ELECTRIC COMPANY, INC.	3	Tied in power from temporary panel to their office trailer and prepped for transformer layout at chiller yard.
Date: 09/11/2021			



Culpepper Construction Company
 Job #: 21006 Santa Rosa School A
 3354 Wallace Lake Road
 Pace, Florida 32571
 8504454824

Group	Company	Workers	Comments
	J MILLER CONSTRUCTION, INC.	1	Brought in fill and built up curb pads in the parking lot.
Date: 09/10/2021			
	J MILLER CONSTRUCTION, INC.	4	Degrubbed and graded east parking lot area. Laid out curb on the north end of the parking lot. Brought in several truck loads of fill for the chiller yard and bus ramp area.
	GULF FENCE & CONSTRUCTION CO	3	Started setting post for permanent fence at north end of the property.
Date: 09/09/2021			
	McKim & Creed	3	McKim and Creed was on site this morning layout out 3 points for the permanent fence line on the north side of the property.
	J MILLER CONSTRUCTION, INC.	4	J Miller continued to build up the grade at the bus ramp and at the chiller pads along side Building F.
	GULF FENCE & CONSTRUCTION CO	4	Gulf Fence mobilized today to start on the permanent fence line. Burke tells me they should be done by mid next week.
Date: 09/08/2021			
	J MILLER CONSTRUCTION, INC.	4	J Miller continued bringing in several truck loads of dirt. J Miller said this dirt was coming off another job and should not cause a CO. J Miller continued grading around bus ramp area as well as tamping down the parking lot pad.
Date: 09/07/2021			
	J MILLER CONSTRUCTION, INC.	3	J Miller continued to cut the parking lot down to subgrade. They brought several truckloads of dirt into the bus ramp earlier to bring it up to grade. They also laid out some of the parking lot curb.
	BARNES ELECTRIC COMPANY, INC.	2	Barnes Electric came out today and staged material and set up their office trailer.
Date: 09/03/2021			
	J MILLER CONSTRUCTION, INC.	2	Grading at parking lot. Grading and filling behind Building F. Curb installer walked the site with Larry at lunch time; said he'll be free in a week and a half, weather allowing.
	BARNES ELECTRIC COMPANY, INC.	2	Install temp power pole and meter
Date: 09/02/2021			
	J MILLER CONSTRUCTION, INC.	2	Grading parking lot. Delivering fill dirt between F and D
Date: 09/01/2021			
	J MILLER CONSTRUCTION, INC.	2	Degrubbing for parking lot
